


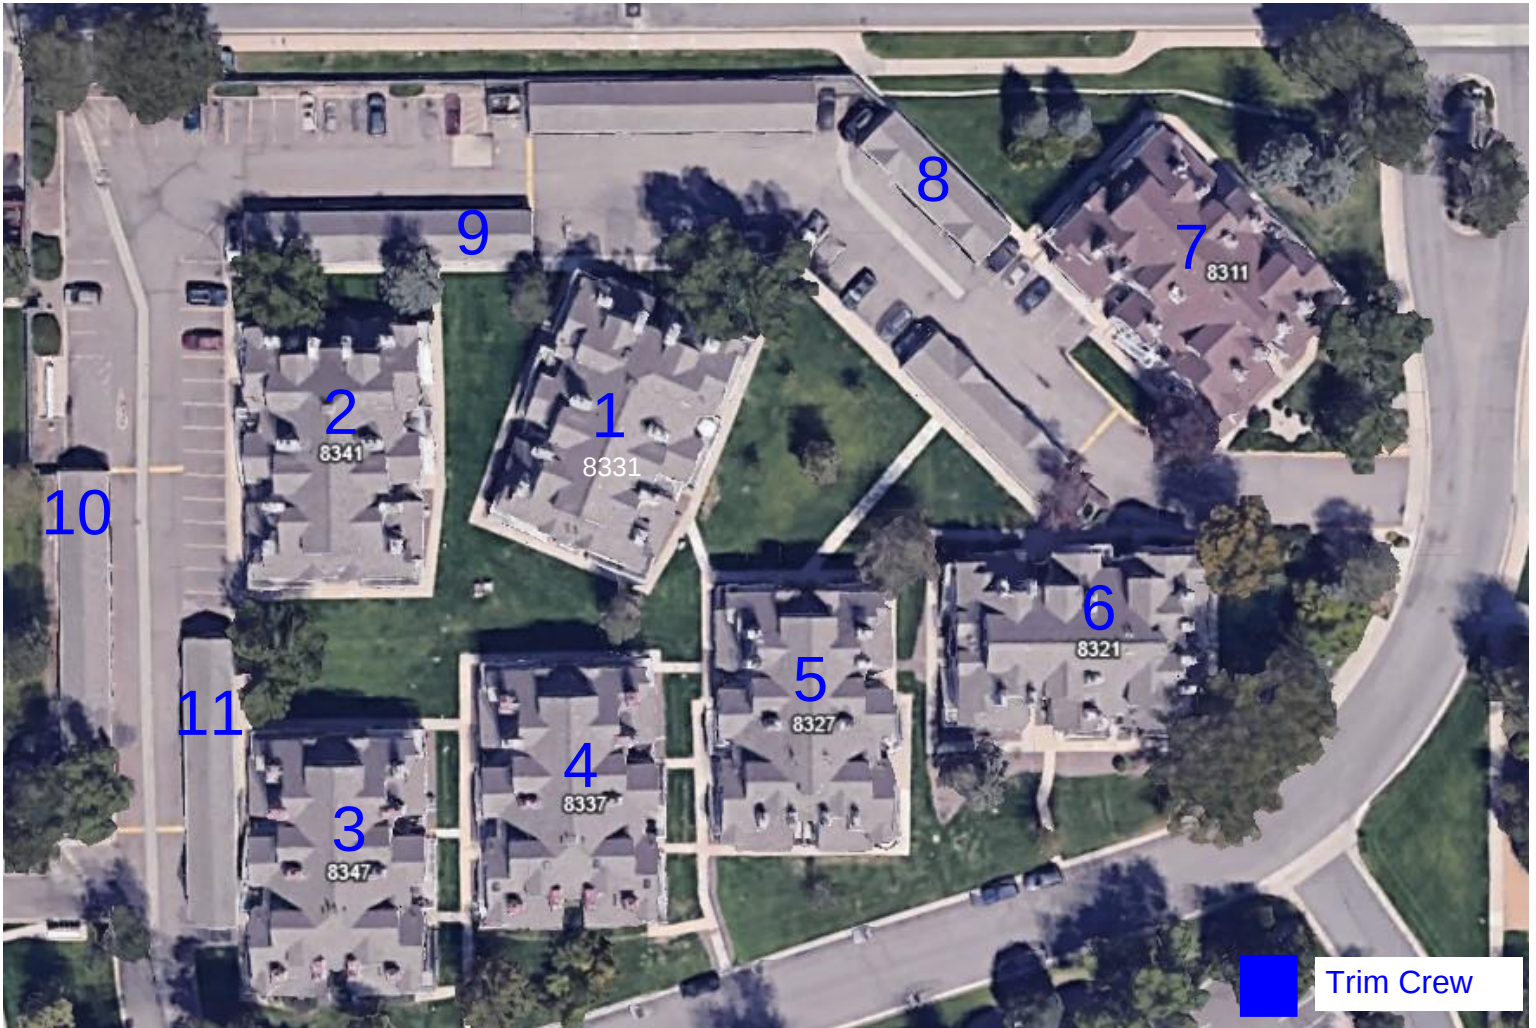

The Reef - Install Sequence

BLDG 1 9/19 - 9/28

BLDG 2 - 2-5 days (trim)
5 days (painter)

BLDG 3 - 2-5 days (trim)
5 days (painter)

BLDG 4 - 2-5 days (trim)
5 days (painter)

BLDG 5 - 2-5 days (trim)
5 days (painter)

BLDG 6 - 2-5 days (trim)
5 days (painter)

BLDG 7 - 2-5 days (trim)
5 days (painter)

Complete at the end or
fit in as needed.

The schedule is set up to allow the trim carpenter to complete one building. Allow the HOA to walk the completed building, add additional items, or sign off on the install.

From there the painter has the following week to paint the building.

The install dates vary due to varying quantities of trim to be replaced on each building.

Building 8331 BLDG 1 has taken the longest due to the entire north elevation siding, vapor barrier and rotten trim being replaced.

The trim crew will work on the following building as the HOA walks and approves the completed previous buildings so work doesn't stop.
